


BRHAT BANGALORE MAHANAGARA PALIKE
INSPECTION REPORT

SI No	Decription	Details	Remarks
1	Name of Work	Improvements to Roads and Drains at Chaakkanahalli Circle to Nanjareddy's House in Ward No. 05 Byatarayanapura Sub Division	
2	Estimate Cost	45.00 Lakhs	
3	Administrative Approved No and Date	617/13-14, Date. 23.12.2013	
4	Technical sanction No. and Date	60/13-14, 23.12.2013	
5	Job Code No. and P Code No.	005-14-000032	
6	Tender Direct Entrested to KRIDL	KRIDL	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	Not Applicable	
8	Tender Approved Details	Not Applicable	
9	Work Order No and Date	371/13-14, Date. 21.02.2014	
10	Stipulation time of Completion	90 Days	
11	Actiual Date of Commencement	21.02.2014	
12	Actiual Date of Completion	28.07.2014	
13	Delay if any	Nil	

	for Delay	Nil	
	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verified	Enclosed	
18	Date of Inspection	12.01.2016	
19	MB No. and Page No.	Mb No.2503 Page No. 250223-238	
20	BR No. and Date	210/31.07.2014	
21	Test Result	Quality Test Report submitted by Civil Tech Consultants and Engineers is verified and Enclosed	
22	Section officer	Sri P A Chandrakanthraju A.E	
23	Sub Division Office	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
a	Work Quality	Satisfactory	
b	Comments	Work completed as per MB	


12/1/16

amelf work :- Improvements to Roads & Drains at Chokkanahally
circle to Nanja Reddy's house in Ward NO-5 of Gyr-Sus. Div.

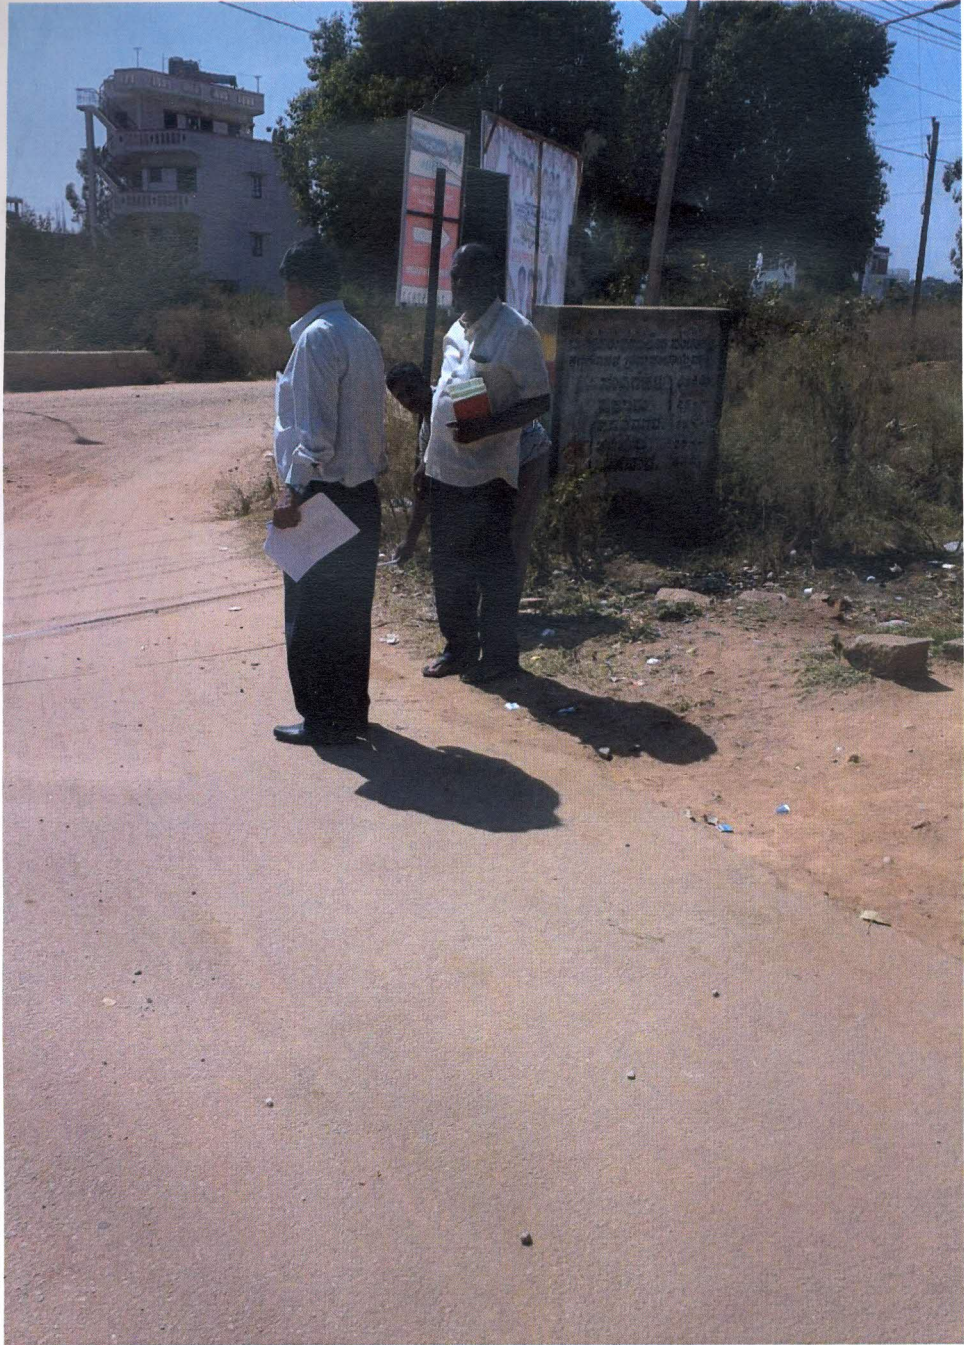

ಆಗಸ್ಟ್
ಸಹಾಯಕ ಅಧ್ಯಯನಾಧಿಕಾರಿ
ಪಿ.ಬಿ.ಎಂ.ಪಿ. ಬೆಂಗಳೂರು ನಗರ ಪುರ ಪಂಚಾಯತ್

— 2 —



24-7

